



152 East Main Street • Forest City, NC 28043
Phone (828) 247-4495 • Fax (828) 247-4498

ENGINEER'S CONSTRUCTION OBSERVATION REPORT

Project: Queenø Gap	Project Number: 2013-002
Contractor: Site Development Corporation	Contact at Site: as noted.
Date: 5/23, 5/24 & 5/26, 2016	Weather Conditions: Workable soils.
Notice to Proceed:	Substantial Completion Date:
Previous Rain Days:	Previous Substantial Completion Date:
Rain Days Since Last Report: Total Rain Days:	Current Substantial Completion Date:

Observations & Notes:

Site inspection for Project 3 and 5 areas: (5/23, 5/24 & 5/26 -2016).

Project 5 ó Work continues on the road re-alignment at the upper part of Project 5 area. Site Development (Jim Worley present) continues to clear and bench the lower part of the new roadbed and fill slope areas. 05/26/2016 note: Subsurface drainage from previous construction encountered. Additional underdrain to intercept the groundwater in the road and slope areas to be provided by Site Development Corp.

Project 3 - Waterline installation continues with T&K Utility (Chris Hendley present) working in Devin Ridge Road at time of inspection. T&K Utility has completed connections of the waterline in other areas on the project that were previously skipped due to other construction activity. T & K Utility to return the roadbed to (19ø) width if disturbed during waterline installation. Post valves and air release valves are being installed in various parts of the project, including Project 2 area that are being prepared for pavement.

Project 3 - Inspection was conducted on 05/26/2016 with David Odom and Rick Connor - areas in Project 3 were observed to be substantially complete less work noted in this report.

The waterline ditch line was proof-rolled on 05/24/2016 in Project 3 road way. Some deflection and minor cracks were observed in various areas. T&K agreed to make corrections to the ditch line and ready the area for paving.

Site Development Corp. - Continue maintenance on ditch lines previously constructed that lack vegetative groundcover. Vegetation needs to be established in all ditch lines, road shoulders and slopes project wide.

Site Inspection for Project 2 & 3 paving: (5/23, 5/24 & 5/26 - 2016).


The road paving of Project 2 and part of Project 3 is scheduled to begin by Caldwell Construction Services (John Caldwell present). Caldwell Construction has started preparation of the stone base course and is adding CABC stone in various areas of the project. Inspection was conducted on 05/24/2016 with Caldwell Construction to evaluate asphalt placement and drainage options. David Odom inspected the site on 05/26/2016 and paving as setup in Project 2 may proceed ó road shoulders may require adjustment following asphalt paving. The Project 3 roadbed will need to be checked by Site Development Corp. for (19ø width) and (6ø) compacted CABC stone depth.

NPDES self-monitoring report is attached.

Reported by: Wayne Watkins, CPESC



Waterline installation of Fire Hydrant assembly and valve by T&K Utility.

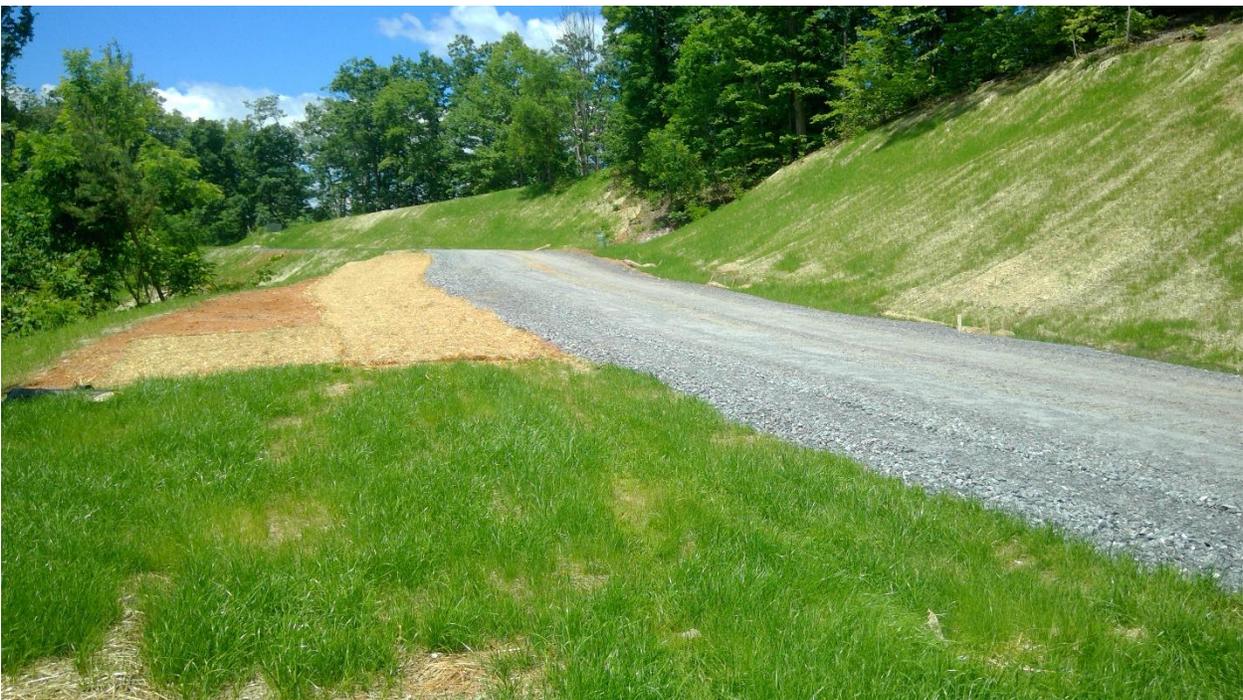

Eamon Drive, Project 5 area of Site Development Corp.



Waterline installation in Devon Ridge Road ó Rock excavation, T&K Utility.



Road bed paving preparation by Caldwell Construction 05/24/2016.
